




# Monthly Progress Report

December 2024

Hempstead Union Free School District

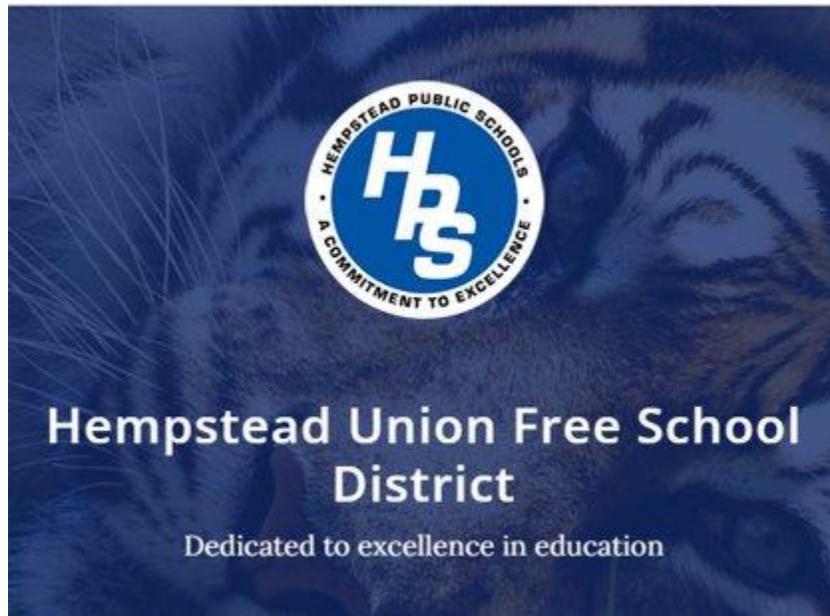

Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress **December 2024**

**Section III** – Work Projected for **January 2025**

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary

### December 2024

#### Project List

- Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – **In Progress**
  - Staircase railings upgrades.
  - Classroom wall upgrades per code.
  - Install eye wash stations.
  - Install new exhaust fans.
  - Install new kitchen Ansul system valves.



## Section II - Work Progress December 2024

### Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
  - Continued removals and installation of new staircase railing in building A.
  - Completed removal of existing walls and replaced with new walls up to ceiling decking. Work took place in rooms c-103 and c-106. Work consisted of framing, insulation, sheetrock, spackle, and paint.
  - Completed concrete portion of exterior ramp by the main entrance. Need to install railings.
  - Completed cutting 6" of wall in pool area to take measurements for handi-lift fabrication.
  - Completed removal and reinstall of 1'x1' ceiling tiles for mechanical contractor.
  - Completed roof openings and roof patching around EF curbs.
- IMC:
  - Completed ductwork roughing in building b copy room, staff dining/covid room, and nurses' office.
  - Completed removal and reinstall of ceiling in areas of work.
  - Completed installation of new Ansul system.
- Maccarone:
  - Completed installation of eye wash stations in nurses' office and boiler room.
  - Completed gas solenoid for Ansul system.
- Locust Valley:
  - Completed all electrical work needed for rebuild of walls in c building, completed electric for Ansul system, and completed replacement of panel in building B.





## Section III - Work Planned January 2025

### **Hempstead UFSD – HS Priority Infrastructure Upgrades**

- Total:
  - Continue to remove existing staircase railings and install new railings in building A and move to building C.
  - Install railing for exterior ramp.
- IMC
  - Install valves in mechanical rooms.
  - Install gas detection system.



## Section IV – Progress Photos

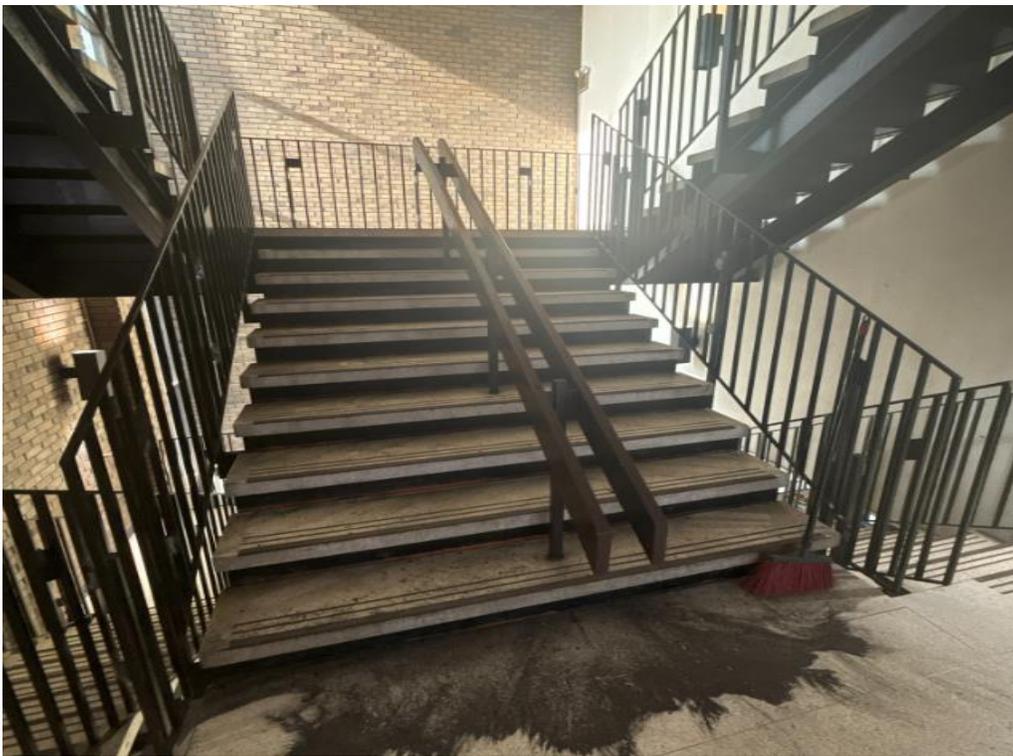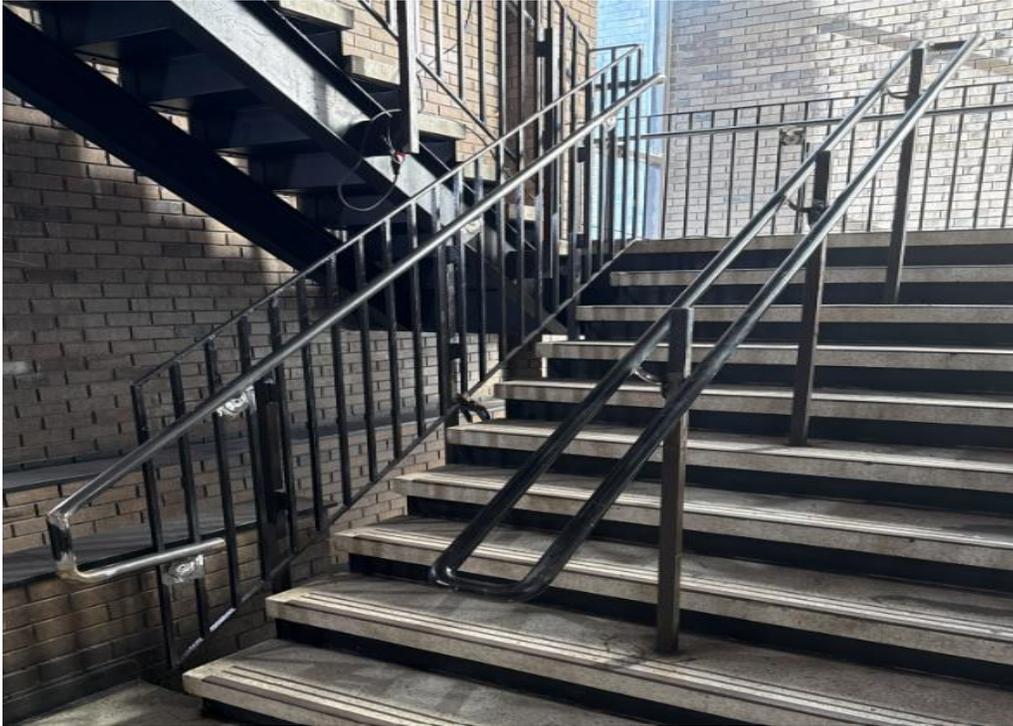

Hempstead HS – Staircase railings




## Section IV – Progress Photos



Hempstead HS – Exterior Ramp



## Section IV – Progress Photos

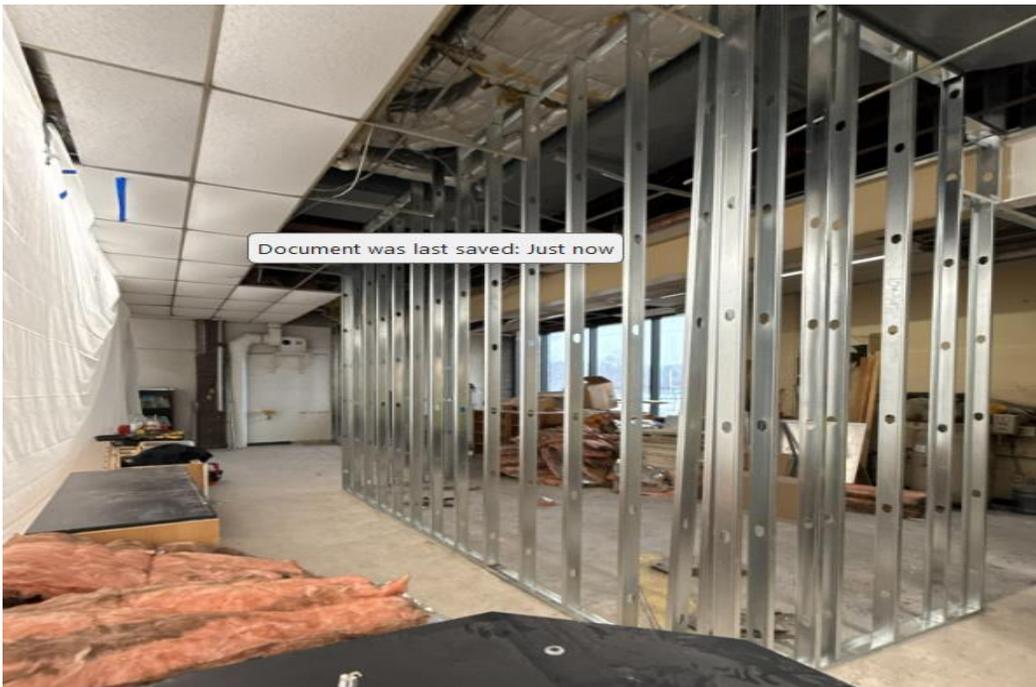

Hempstead HS – C building classrooms




## Section IV – Progress Photos



Hempstead HS – C building classrooms



## Section IV – Progress Photos

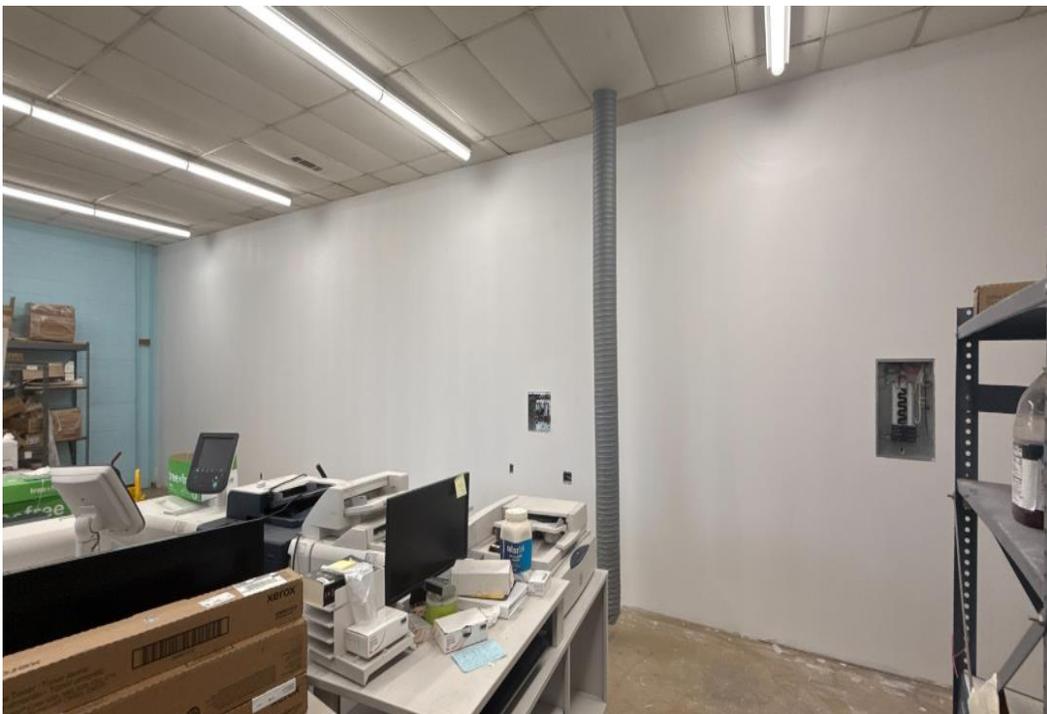

Hempstead HS – C building classrooms



## Section IV – Progress Photos



Hempstead HS – Ductwork roughing



## Section IV – Progress Photos



Hempstead HS – Ductwork roughing



## Section IV – Progress Photos



Hempstead HS – Ansul system



## Section IV – Progress Photos



Hempstead HS – Eye wash stations




## Section V – Workforce Summary – Company/Hours

### December 2024

#### Manpower Chart

▼ MANPOWER GRAPH

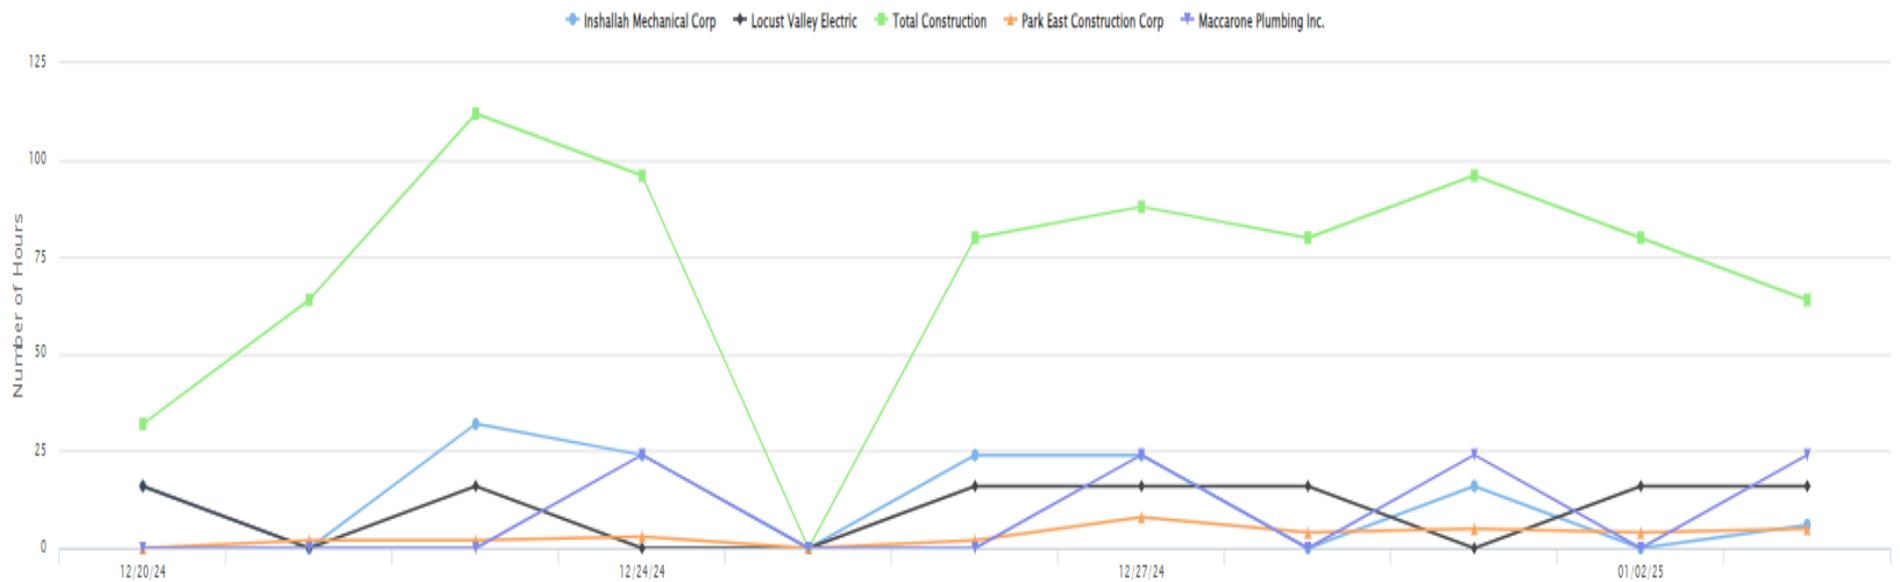



Hempstead Union Free School District  
December 2024

**End of Progress Report**
