




Monthly Progress Report

November 2023

Hempstead Union Free School District

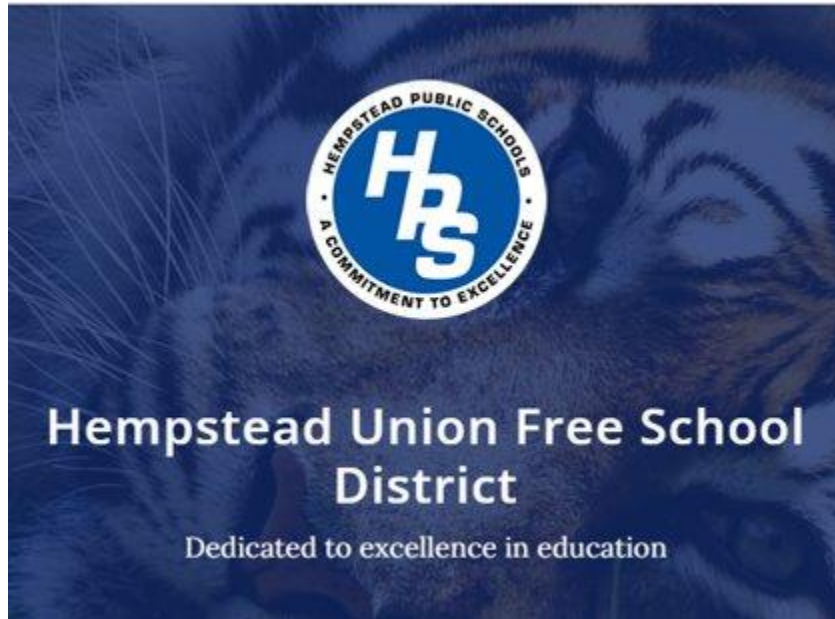

Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress November 2023

Section III – Work Projected for December 2023

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

November 2023

Project List

- Hempstead UFSD - HS Infrastructure & Site Construction
- Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS
- Hempstead UFSD – Phase 1 Roof Replacements
- Hempstead UFSD – Phase 1 Window Replacements



Section II - Work Progress November 2023

Hempstead UFSD - HS Infrastructure & Site Construction

- Laser Industries Inc.:
 - Installed shotput.
 - Reordered discus circle came in the wrong size.
- Nickerson Corp.:
 - All work completed.

Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS

- Gatz Sitework & Landscape Construction:
 - All work completed.

Hempstead UFSD – Phase 1 Roof Replacements

- More Contracting & Consulting. (High School):
 - Completed Cedar wall siding.
 - Completed metal copings on cedar wall.
 - Started brickwork change order. Completed south wall.
 - Started working on the punch list.
- More Contracting & Consulting. (Paterson ES):
 - Completed gutters & leaders.
 - Completed metal panels and copings.
 - Completed copper cap flashings.
 - Installed Skylight.
 - Delivered chimney cap.



Section II - Work Progress

November 2023

- More Contracting & Consulting. (ABGS MS):
 - Completed metal panels and copings.
 - Completed gas main brackets.
 - Completed installation of ladder.

Hempstead UFSD – Phase 1 Window Replacements

- Arrow Steel:
 - Delivered storage containers.



Section III - Work Planned December 2023

Hempstead UFSD - HS Infrastructure & Site Construction

- Complete any open change orders.
- Start on closeout documentation.

Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS

- No work planned.

Hempstead UFSD – Phase 1 Roof Replacements

- More Contracting & Consulting. (High School)
 - Complete punch list items.
 - Complete open change orders.
 - Start on closeout documentation.
- More Contracting & Consulting. (Paterson ES)
 - Install chimney cap.
 - Complete punch list items.
 - Start on closeout documentation.
- More Contracting & Consulting. (ABGS MS)
 - Complete punch list items.
 - Start on closeout documentation.

Hempstead UFSD – Phase 1 Window Replacements

- Arrow Steel:
 - Deliver windows.
 - Start window replacement.



Section IV – Progress Photos



Hempstead UFSD - HS Infrastructure & Site Construction



Section IV – Progress Photos



Hempstead UFSD - HS Infrastructure & Site Construction



Section IV – Progress Photos



Hempstead UFSD – Phase 1 Roof Replacements (High School)



Section IV – Progress Photos




Hempstead UFSD – Phase 1 Roof Replacements (Paterson & ABGS)



Section V – Workforce Summary – Company/Hours

Hempstead UFSD - HS Infrastructure & Site Construction November 2023

▼ MANPOWER GRAPH

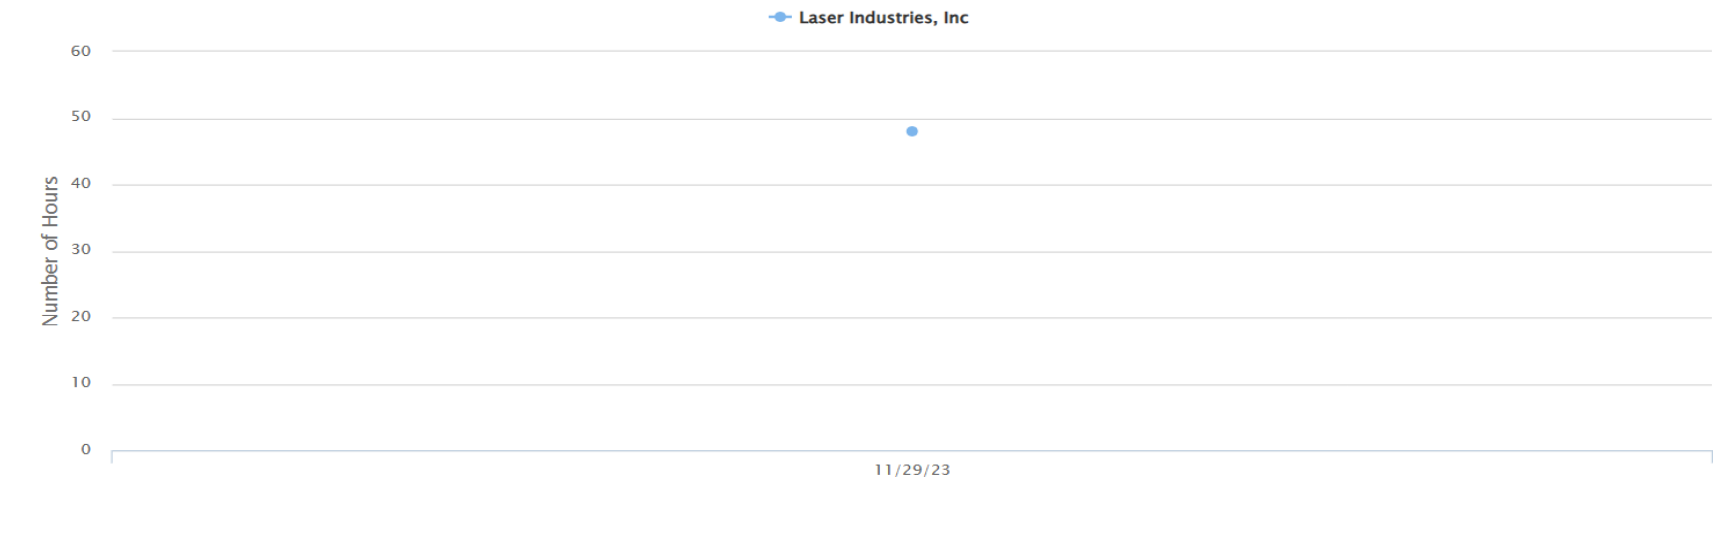




Section V – Workforce Summary – Company/Hours

Hempstead UFSD – Phase 1 Roof Replacements

November 2023

▼ MANPOWER GRAPH

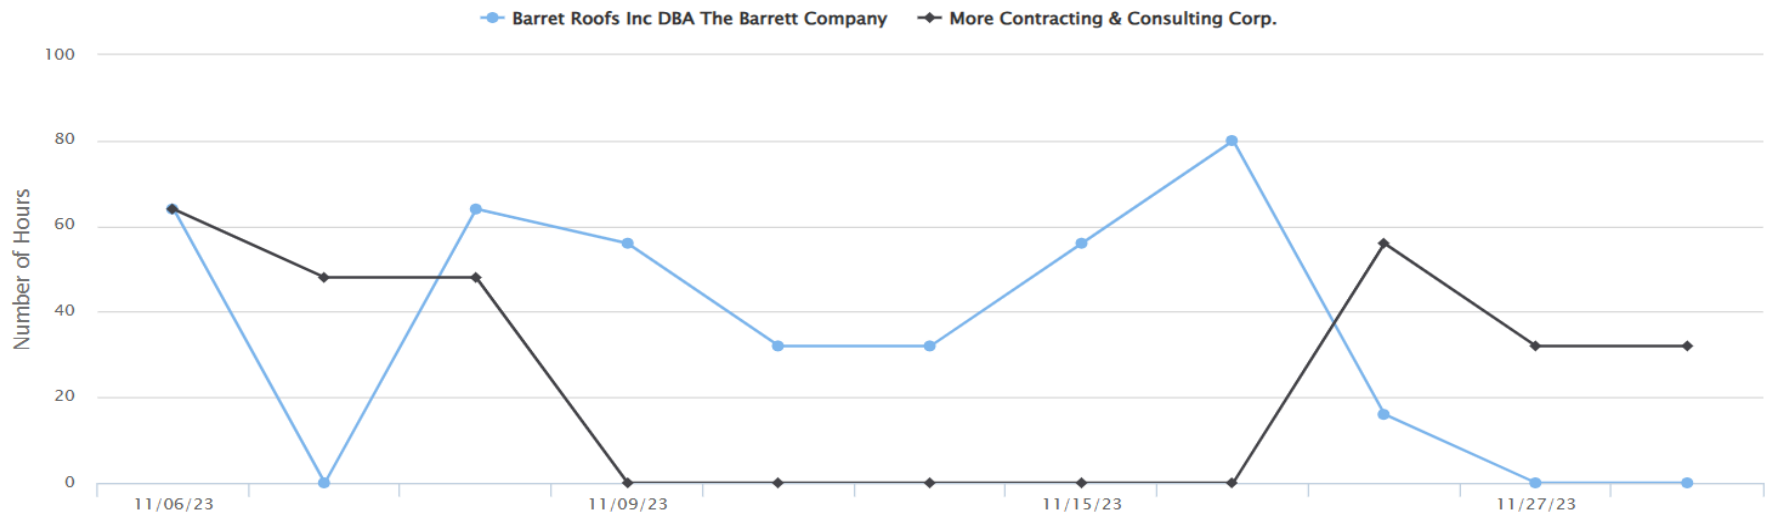



Hempstead Union Free School District
November 2023

End of Progress Report
