




Monthly Progress Report

January 2024

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **January 2024**

Section III – Work Projected for **February 2024**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary January 2024

Project List

- Hempstead UFSD - HS Infrastructure & Site Construction - **Complete**
- Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS - **Complete**
- Hempstead UFSD – Phase 1 Roof Replacements - **Complete**
- Hempstead UFSD – Phase 1 Window Replacements – **In progress**



Section II - Work Progress January 2024

Hempstead UFSD - HS Infrastructure & Site Construction

- Working on finalizing all closeout documentation.

Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS

- Working on finalizing all closeout documentation.

Hempstead UFSD – Phase 1 Roof Replacements

- Working on finalizing all closeout documentation.

Hempstead UFSD – Phase 1 Window Replacements

- **Obama ES:**
- Arrow Steel:
 - Completed installation of all windows throughout school.
 - Installed window film on all windows.
 - Started to caulk around all window frames.
- **Jackson Main ES:**
- Arrow Steel:
 - Delivered storage containers to school.
 - All windows were delivered.
 - Started removal and installation of windows.
 - Completed 5 rooms.



Section III - Work Planned February 2024

Hempstead UFSD - HS Infrastructure & Site Construction

- Complete closeout documentation.

Hempstead UFSD – Phase 1 Roof Replacements

- More Contracting & Consulting. (High School)
 - Complete closeout documentation.
- More Contracting & Consulting. (Paterson ES)
 - Complete closeout documentation.
- More Contracting & Consulting. (ABGS MS)
 - Complete closeout documentation.

Hempstead UFSD – Phase 1 Window Replacements

- **Obama ES:**
- Arrow Steel:
 - Continue installation of caulking around windows.
- **Jackson Main ES:**
- Arrow Steel:
 - Continue removal and installation of windows throughout school.



Section IV – Progress Photos



Hempstead UFSD – Phase 1 Window Replacements - Obama ES



Section IV – Progress Photos



Hempstead UFSD – Phase 1 Window Replacements – Jackson Main ES




Section V – Workforce Summary – Company/Hours

Hempstead UFSD – Phase 1 Window Replacements

January 2024

Daily Log Manpower Report

MANPOWER GRAPH

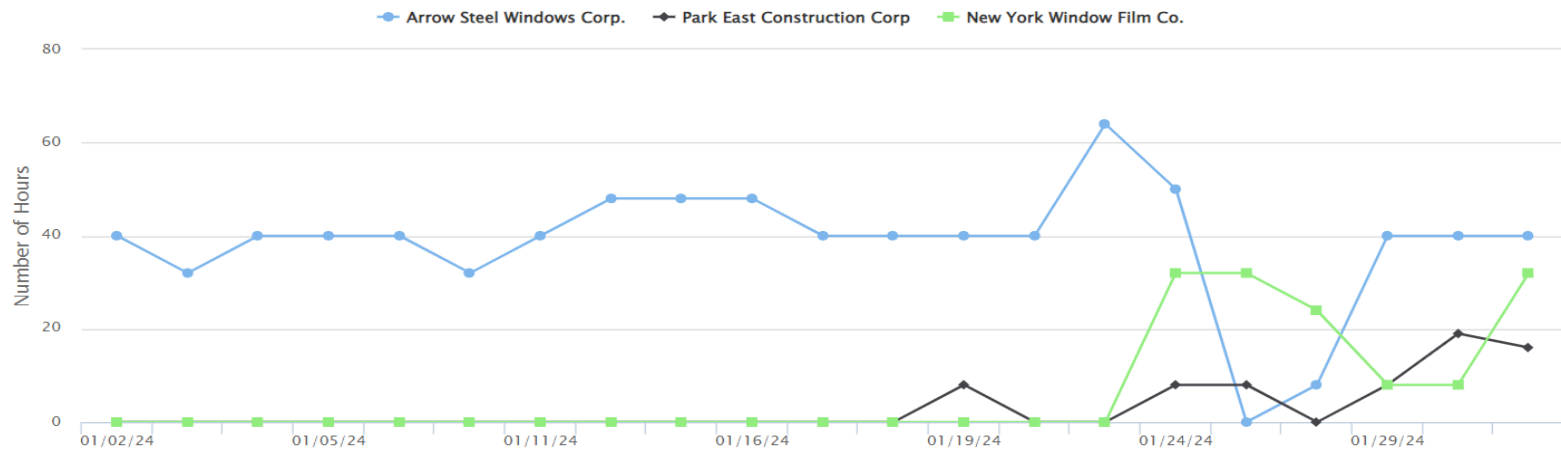

Section V – Workforce Summary – Company/Hours



Hempstead Union Free School District

January 2024

End of Progress Report
